


Land Acquisition Progress – As of Sept 2, 2011

- 485 Potential parcels identified
- 64 No action taken
- 102 Eliminated
- 319 Acquisitions required
 - » 40 CLEAR
 - » 10 In Condemnation
 - » 12 In Negotiations
 - » 90 In Appraisal
 - » 55 In R/W Engineering
 - » 112 In Title Research


Land Acquisition Progress

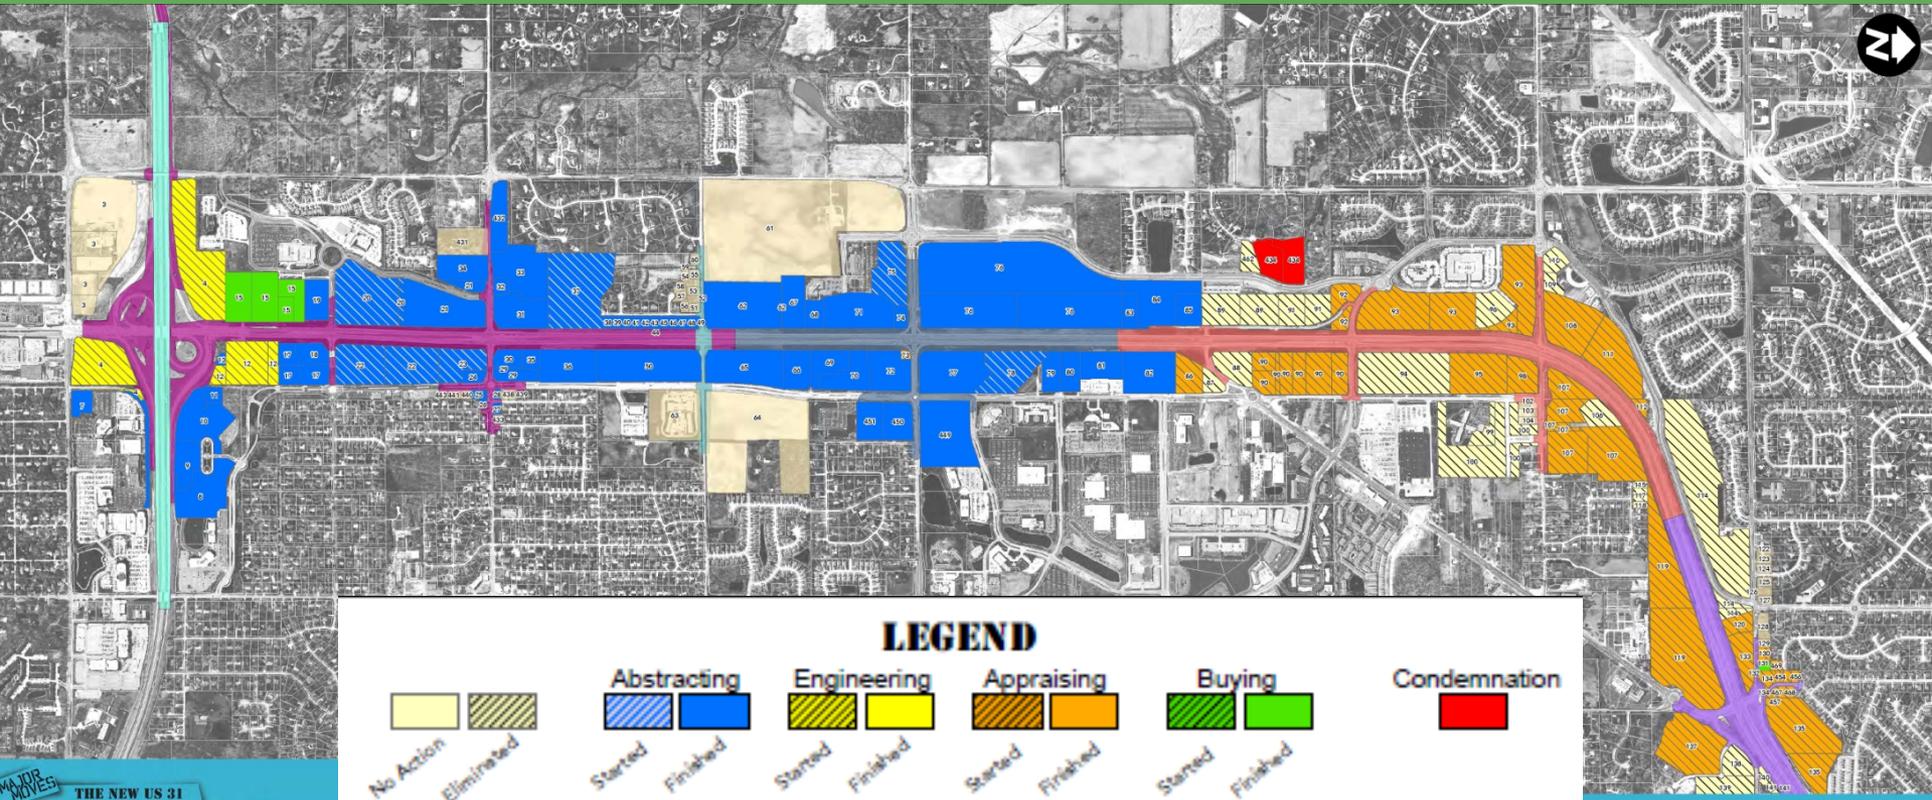

RIGHT-OF-WAY PROGRESS - SHEET 1 OF 3

SEPTEMBER 2, 2011


Land Acquisition Progress

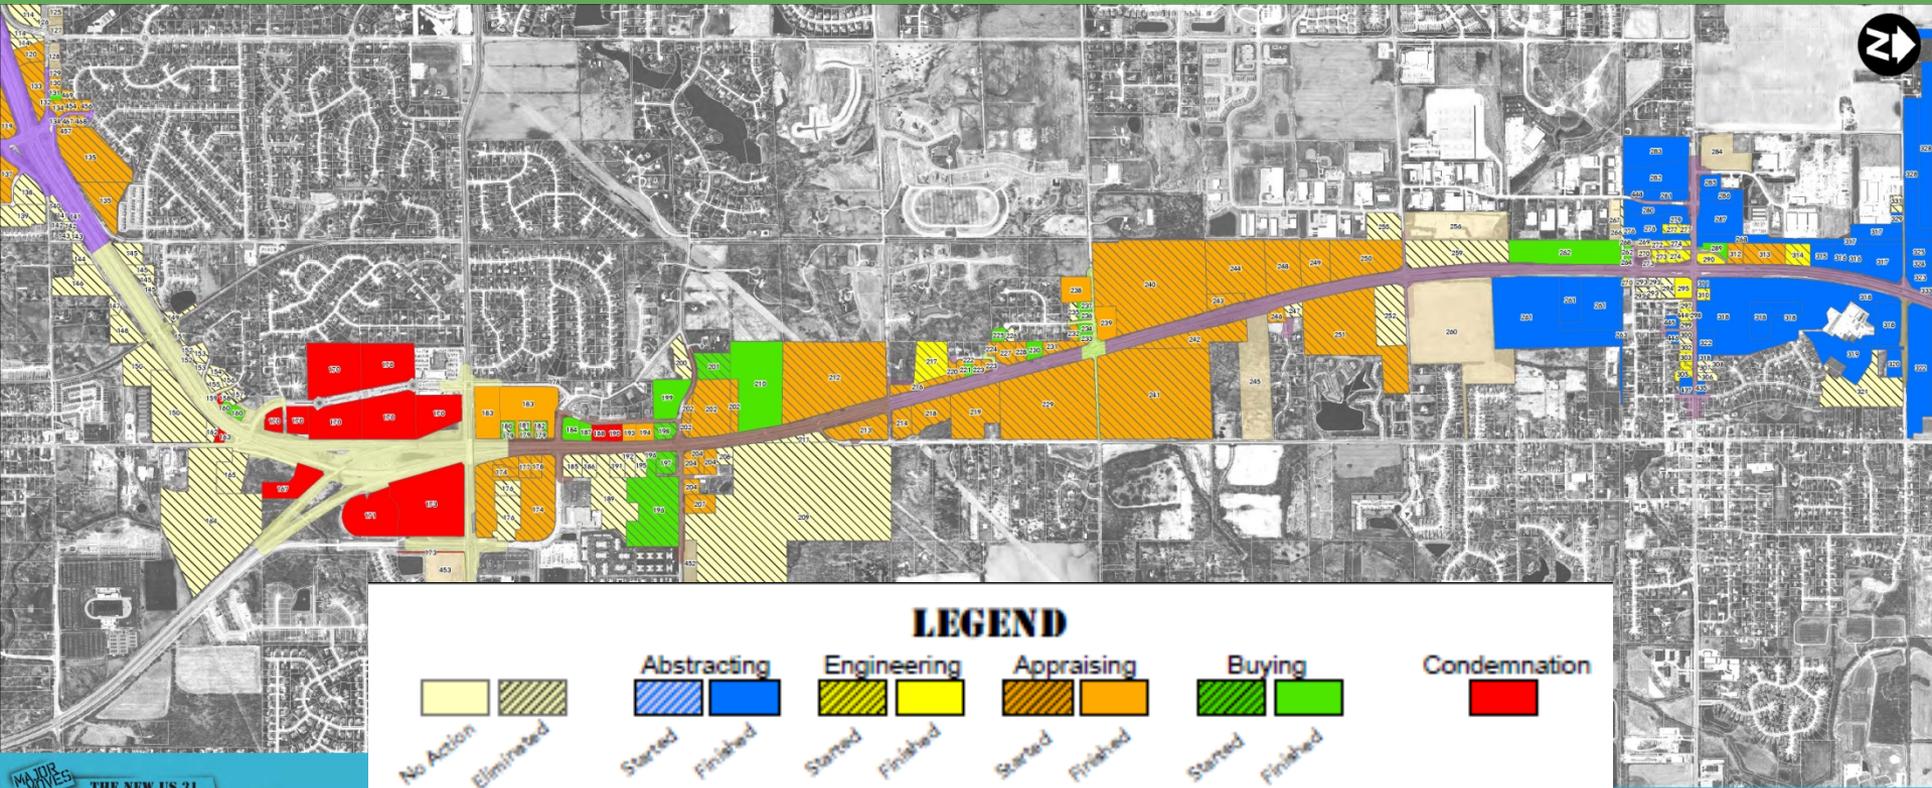

RIGHT-OF-WAY PROGRESS - SHEET 2 OF 3

SEPTEMBER 2, 2011


Land Acquisition Progress

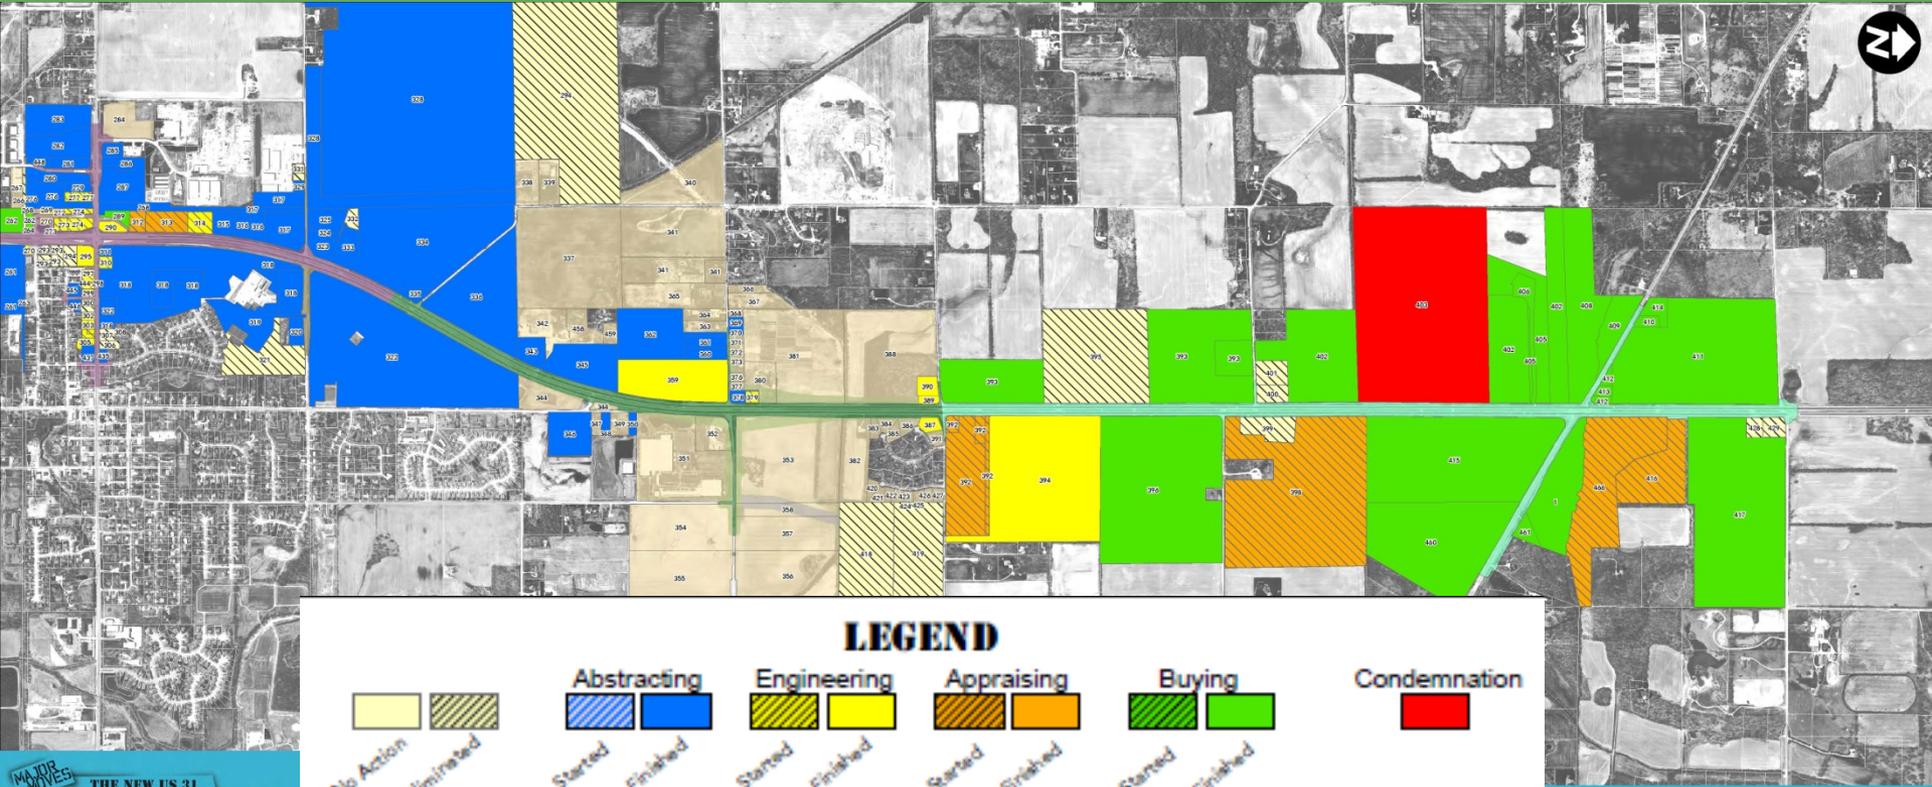

RIGHT-OF-WAY PROGRESS - SHEET 3 OF 3

SEPTEMBER 2, 2011

Land Acquisition Projected to August 2012

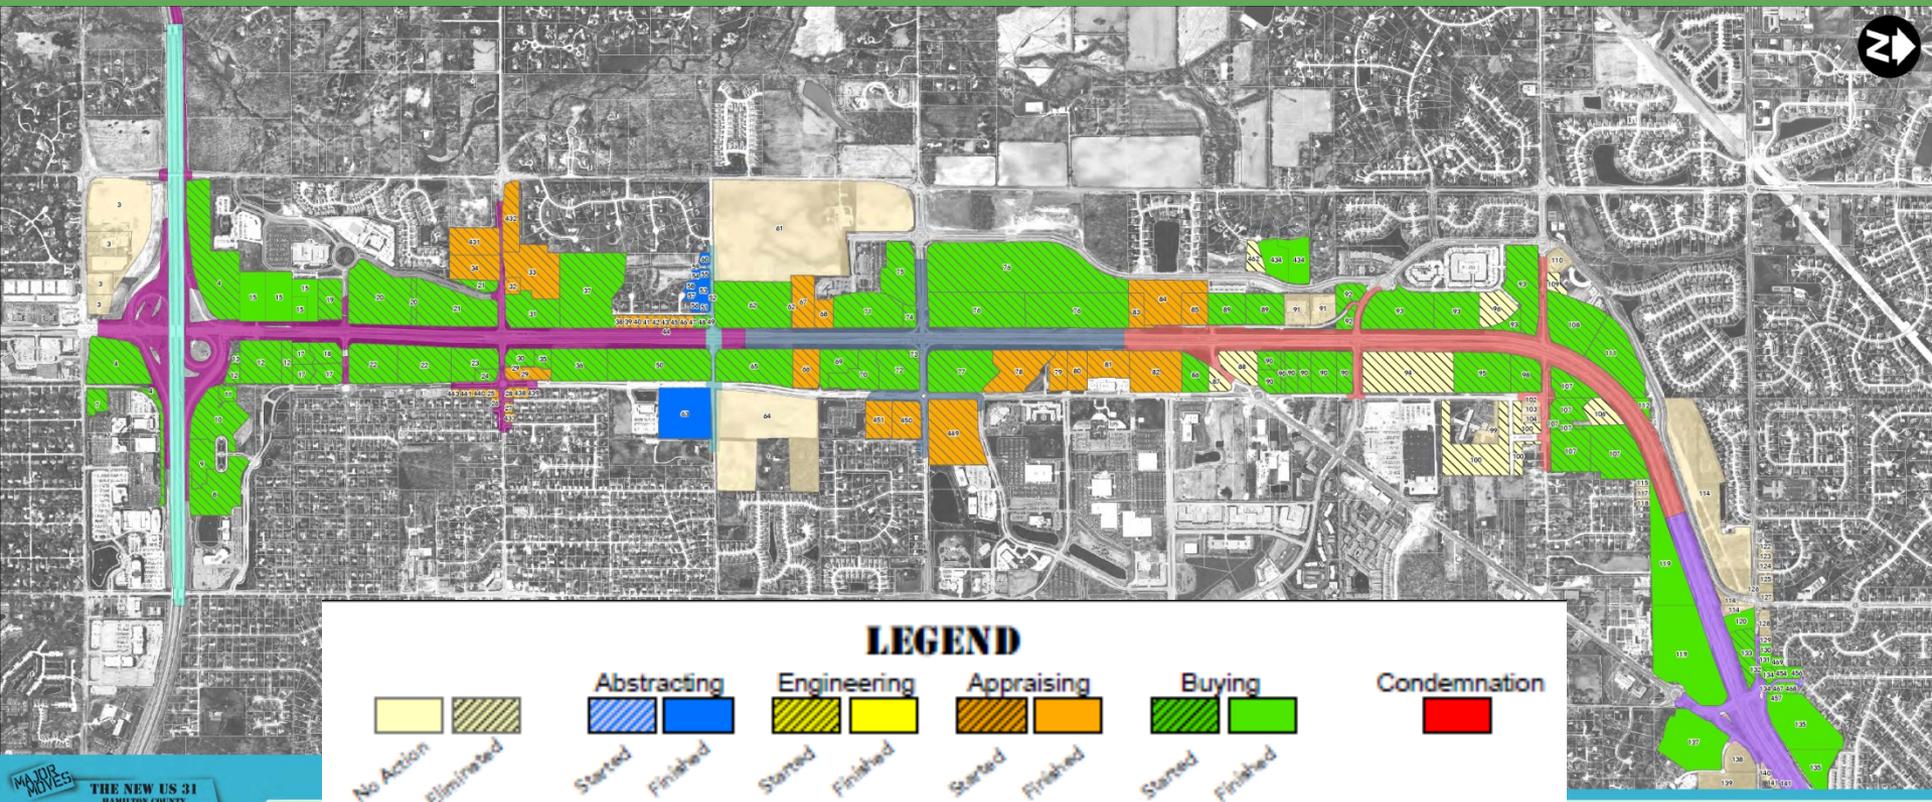


RIGHT-OF-WAY PROGRESS - SHEET 1 OF 3

PROJECTED AUGUST 1, 2012




Land Acquisition Projected to August 2012

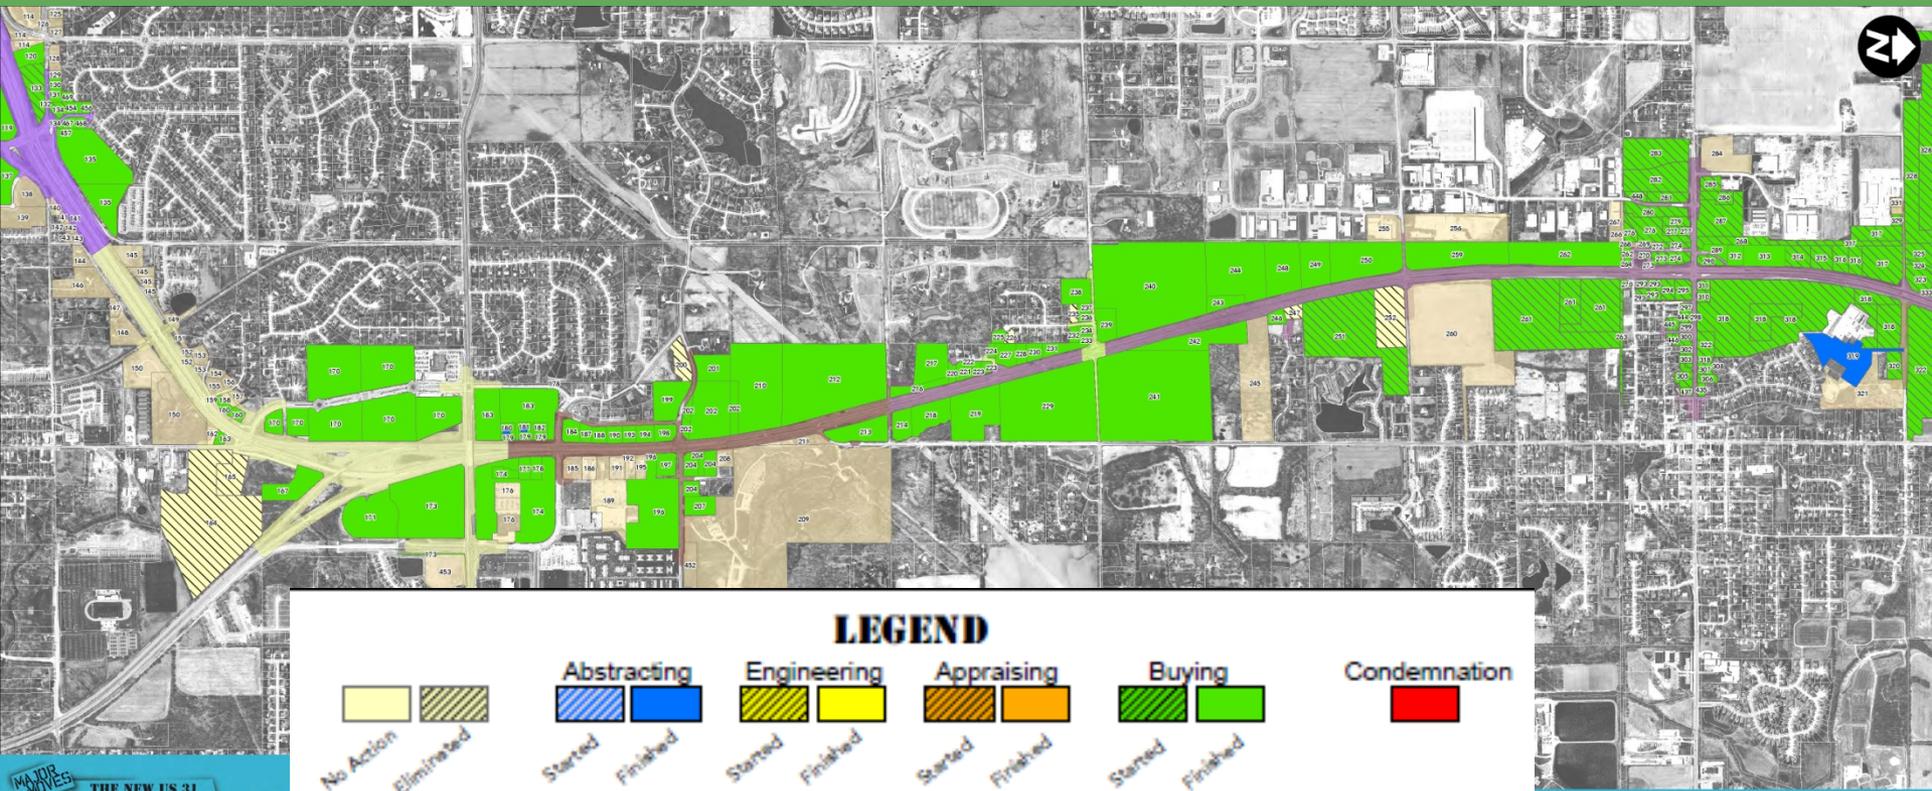

RIGHT-OF-WAY PROGRESS - SHEET 2 OF 3

PROJECTED AUGUST 1, 2012

Land Acquisition Projected to August 2012

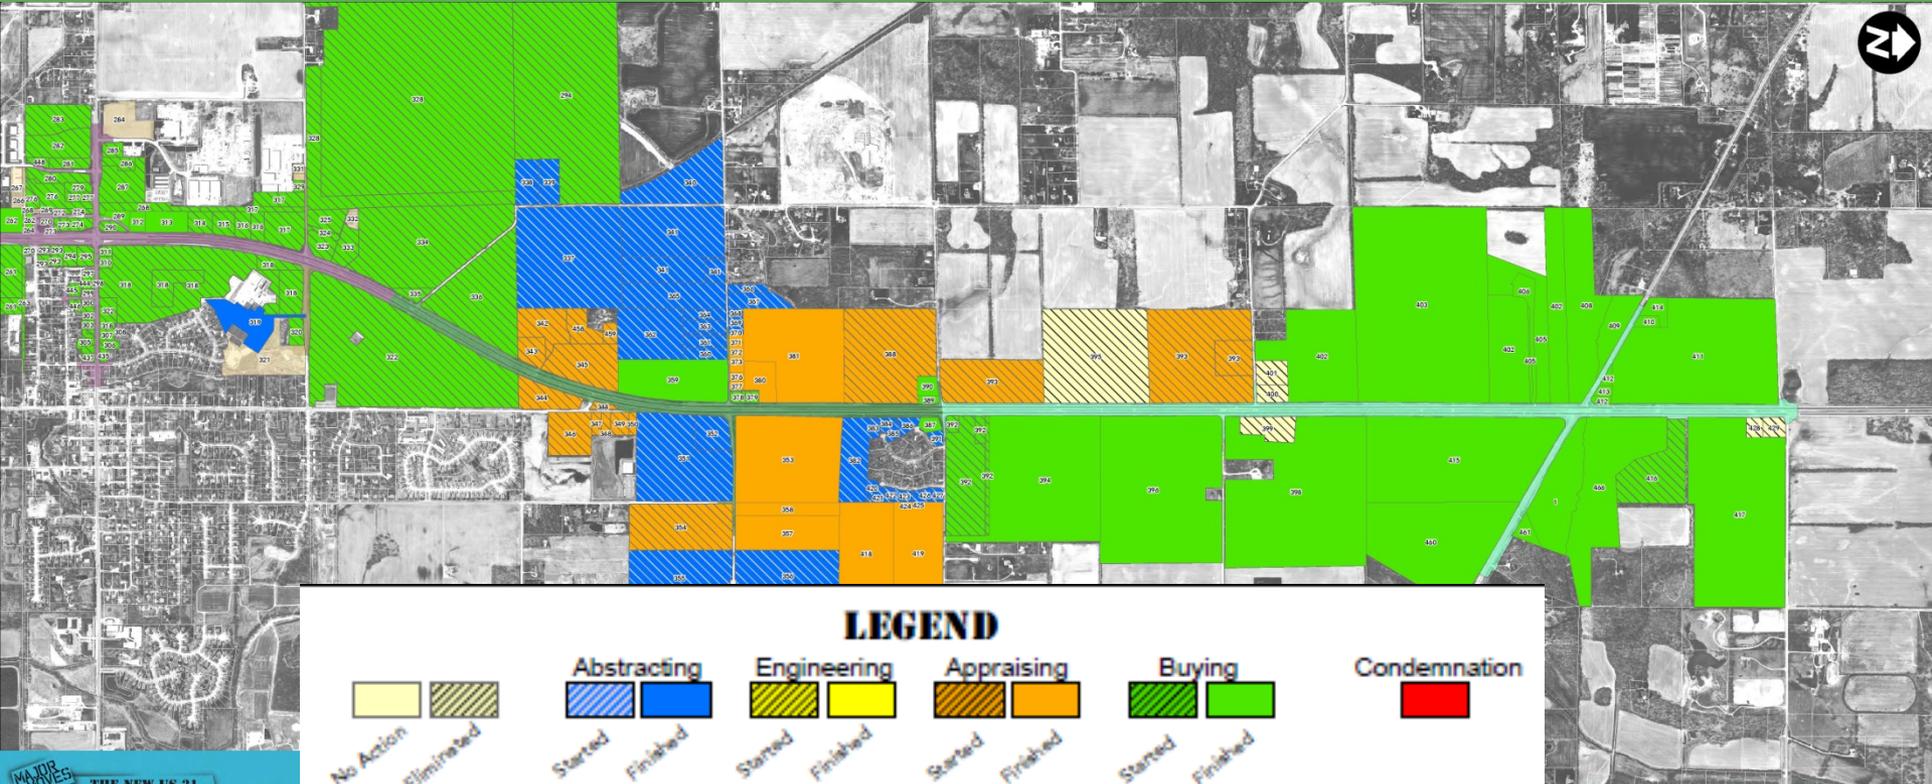

RIGHT-OF-WAY PROGRESS - SHEET 3 OF 3

PROJECTED AUGUST 1, 2012
